

SE Lab 2

Deana Naveen A
PES1UG24AM077

1. Backlog

Spaces / SE-Lab

SL board ...

Summary Timeline Active sprints **Backlog** Calendar List Forms Development Docs +

Search backlog Version Epic Quick filters


Epic


- No epic
- Epic 1: Equipment Reservation
- Epic 2: Equipment Management
- Usage Tracking & Accountability
- Security & Performance
- + Create epic

Create a whiteboard to plan your work Try


☒	SL-5 Story 1.1: View Availability	Epic 1: Eq...	To Do	3	^	
☒	SL-6 Story 1.2: Reserve Equipment Slot	Epic 1: Eq...	To Do	8	^	
☒	SL-7 Story 1.3: Cancel Reservation	Epic 1: Eq...	To Do	3	^	
☒	SL-8 Story 2.1: Update Equipment Status	Epic 2: Eq...	To Do	3	^	
☒	SL-9 Story 2.2: Block Unusable Equipment	Epic 2: Eq...	To Do	2	^	
☒	SL-10 Story 3.1: Record Check-out and Return	Usage Tr...	To Do	5	=	
☒	SL-11 Story 3.2: Flag Late Returns	Usage Tr...	To Do	5	=	
☒	SL-12 Story 3.3: Apply Disciplinary Restrictions	Usage Tr...	To Do	3	=	
☒	SL-13 Story 4.1: Role-Based Access	Security ...	To Do	5	^	
☒	SL-14 Story 4.2: Concurrent Booking Safety	Security ...	To Do	8	^	


2. Sprint 1

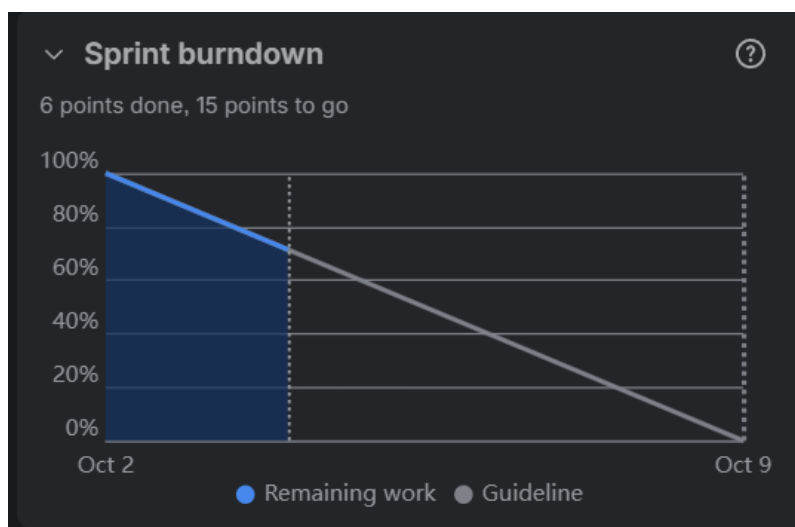

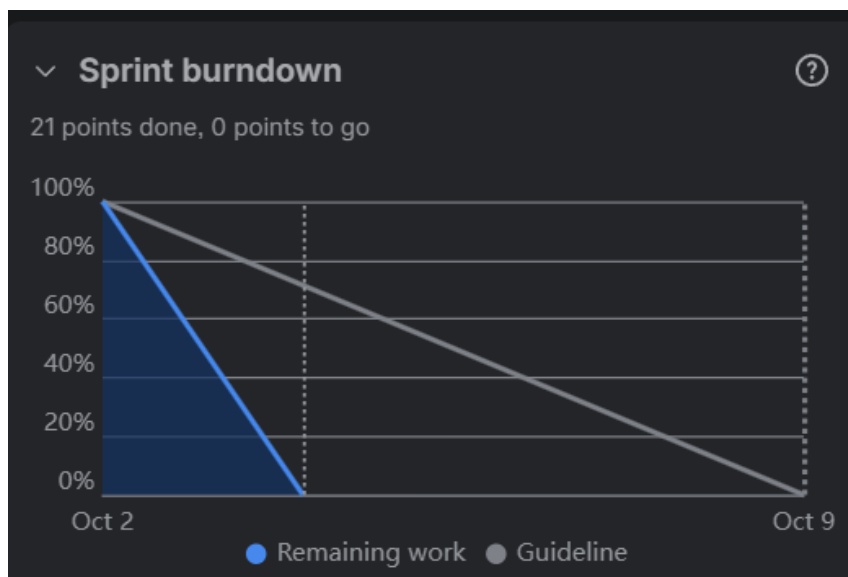

3. Sprint 2

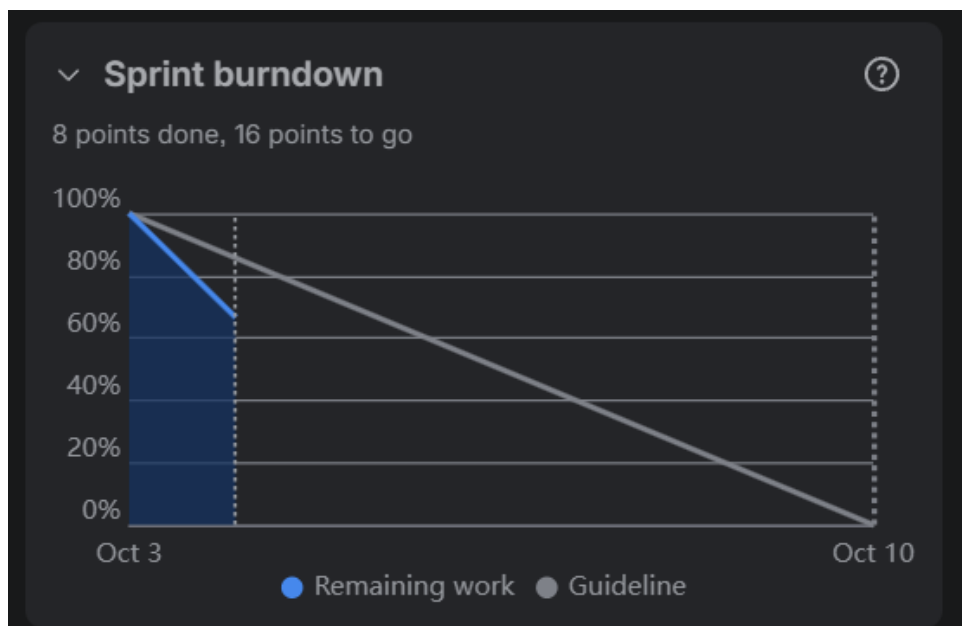

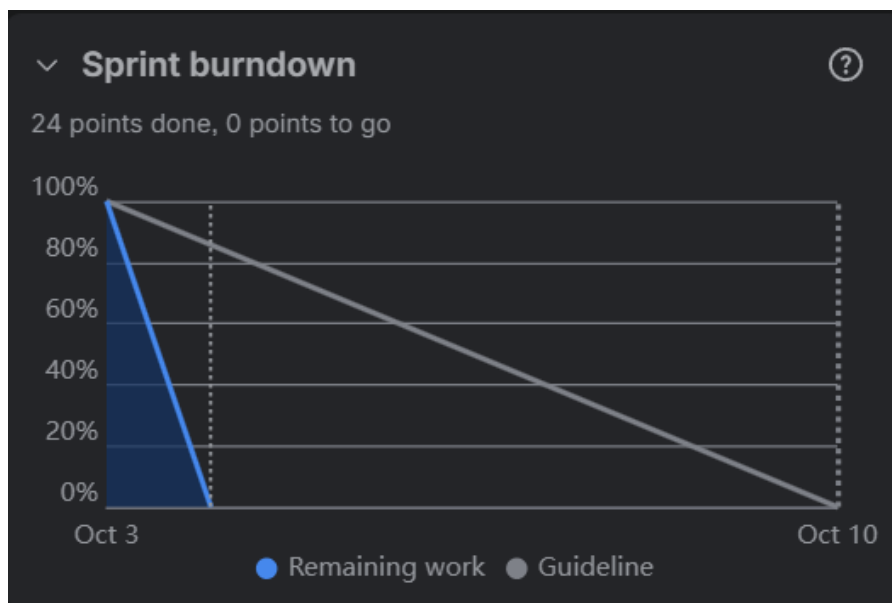

Reflection Answers

1. Did your estimations reflect the actual effort?

Mostly yes. Stories 1.2 (Reserve Equipment Slot) and 4.2 (Concurrent Booking Safety) got 8 points each because they involve slot locking, validation and race conditions. Simple stories like 2.2 (Block Unusable Equipment) got 2 points. Since this was a simulated sprint, the actual effort was represented by how long each card stayed In Progress, and the larger stories were the ones that took longest to move to Done.

2. Was your backlog well-prioritized?

Yes. I gave High priority to the core booking flow and the things it depends on: viewing availability, reserving, cancelling, equipment status, role-based access and concurrency safety. Usage tracking and late-return enforcement (Epic 3) are Medium because they add accountability but don't block booking.

3. How did your simulated sprint align with your plan?

Both sprints were completed in full. Sprint 1 committed 21 points (1.1, 1.2, 2.1, 2.2, 4.1) and delivered 21. Sprint 2 committed 24 points (1.3, 3.1, 3.2, 3.3, 4.2) and delivered 24. Work moved through To Do → In Progress → Done in stages. The mid-sprint views show partial progress before the final completion.

4. What insights did the burndown chart give about your team's capacity?

In both sprints the remaining-work line (blue) dropped below the guideline (grey) and reached 0 well before the sprint end date. That means the work was finished ahead of the linear pace. The steep, cliff-like drops also show that work was completed in a few large moves instead of steadily day by day, which is a limitation of simulating a one-week sprint in a short time.
